


ID	Task Name	Duration	Start	Finish	2021		Half 1, 2022			Half 2, 2022			Half 1, 2023			Half 2, 2023			Half 1, 2024			Half 2, 2024			Half 1, 2025
					S	N	J	M	M	J	S	N	J	M	M	J	S	N	J	M	M	J	S	N	J
1	Executed Agreement / NTP	2 days	Tue 11/23/21	Wed 11/24/21																					
2	Project Initiation / Kick-Off	4 days?	Fri 1/7/22	Wed 1/12/22																					
3	Review Budget	2 days	Thu 1/6/22	Fri 1/7/22																					
4	Meeting in Field to Review Service Area	2 days	Mon 1/10/22	Tue 1/11/22																					
5	Design & Permitting	585 days	Wed 1/12/22	Wed 4/10/24																					
6	Field Work	135 days	Mon 2/14/22	Fri 8/19/22																					
7	Prepare Preliminary Plan Sheets	10 days	Mon 8/22/22	Fri 9/2/22																					
8	Review Field Work	10 days	Fri 9/2/22	Thu 9/15/22																					
9	Update Plans with First Energy Approved Make-Ready	15 days	Fri 1/19/24	Thu 2/8/24																					
10	Final Construction Plan Package	10 days	Fri 2/9/24	Thu 2/22/24																					
11	First Energy Pole Agreement Process	210 days	Fri 3/31/23	Thu 1/18/24																					
12	Pole Attachment User Agreement Process	1 day	Fri 3/31/23	Fri 3/31/23																					
13	Citynet Coordination With First Energy	50 days	Thu 7/13/23	Wed 9/20/23																					
14	Pole Data Sheets into First Energy SPANS Portal	21 days	Thu 9/21/23	Thu 10/19/23																					
15	First Energy Make Ready Engineering Review	45 days	Fri 10/20/23	Thu 12/21/23																					
16	Coordinate with First Energy on Comments and Finalization	20 days	Fri 12/22/23	Thu 1/18/24																					
17	Environmental Clearances	491 days	Wed 1/12/22	Wed 11/29/23																					
18	SHPO Coordination	30 days	Wed 1/12/22	Tue 2/22/22																					
19	USACE Coordination	30 days	Wed 1/12/22	Tue 2/22/22																					
20	WVDNR/USFWS/RTE Coordination	30 days	Wed 1/12/22	Tue 2/22/22																					
21	USFS Special Use Permit	252 days	Tue 11/1/22	Wed 10/18/23																					
22	Development Office Environmental Review	30 days	Thu 10/19/23	Wed 11/29/23																					
23	WVDOH (MM109 Permits)	408 days	Fri 9/16/22	Wed 4/10/24																					
24	Profile Road Crossings	5 days	Fri 9/16/22	Thu 9/22/22																					
25	MM109 Permit Application	2 days	Fri 2/9/24	Mon 2/12/24																					
26	Submit MM109 Permit to WVDOH	1 day	Tue 2/13/24	Tue 2/13/24																					
27	Permit Review by WVDOH	30 days	Wed 2/14/24	Tue 3/26/24																					
28	WVDOH Comment Review/Comment Process	10 days	Wed 3/27/24	Tue 4/9/24																					
29	Secure WVDOH MM109 Permit(s)	0 days	Wed 4/10/24	Wed 4/10/24																					
30	Notice to Proceed / Release of Funds from Funding Agency	0 days	Wed 4/10/24	Wed 4/10/24																					
31	Preparation of Construction Documents	40 days	Wed 1/17/24	Tue 3/12/24																					
32	Prepare Bidding Documents & Project Manual	30 days	Wed 1/17/24	Tue 2/27/24																					
33	QA / QC of Construction Documents	10 days	Wed 2/28/24	Tue 3/12/24																					
34	Bidding & Negotiating	76 days	Wed 4/10/24	Wed 7/24/24																					
35	Obtain Authorization to Advertise	0 days	Wed 4/10/24	Wed 4/10/24																					
36	Request for Information Bidding Phase	30 days	Wed 4/10/24	Tue 5/21/24																					
37	Advertise for Bidding	30 days	Wed 4/10/24	Tue 5/21/24																					
38	Bid Opening	0 days	Wed 5/22/24	Wed 5/22/24																					
39	Bid Hold & Review	30 days	Wed 6/12/24	Tue 7/23/24																					
40	Issue the Notice of Award	0 days	Wed 7/24/24	Wed 7/24/24																					
41	Execute Contracts	0 days	Wed 7/24/24	Wed 7/24/24																					
42	Issue Notice to Proceed	1 day	Wed 7/24/24	Wed 7/24/24																					
43	Construction	125 days	Thu 7/25/24	Wed 1/15/25																					

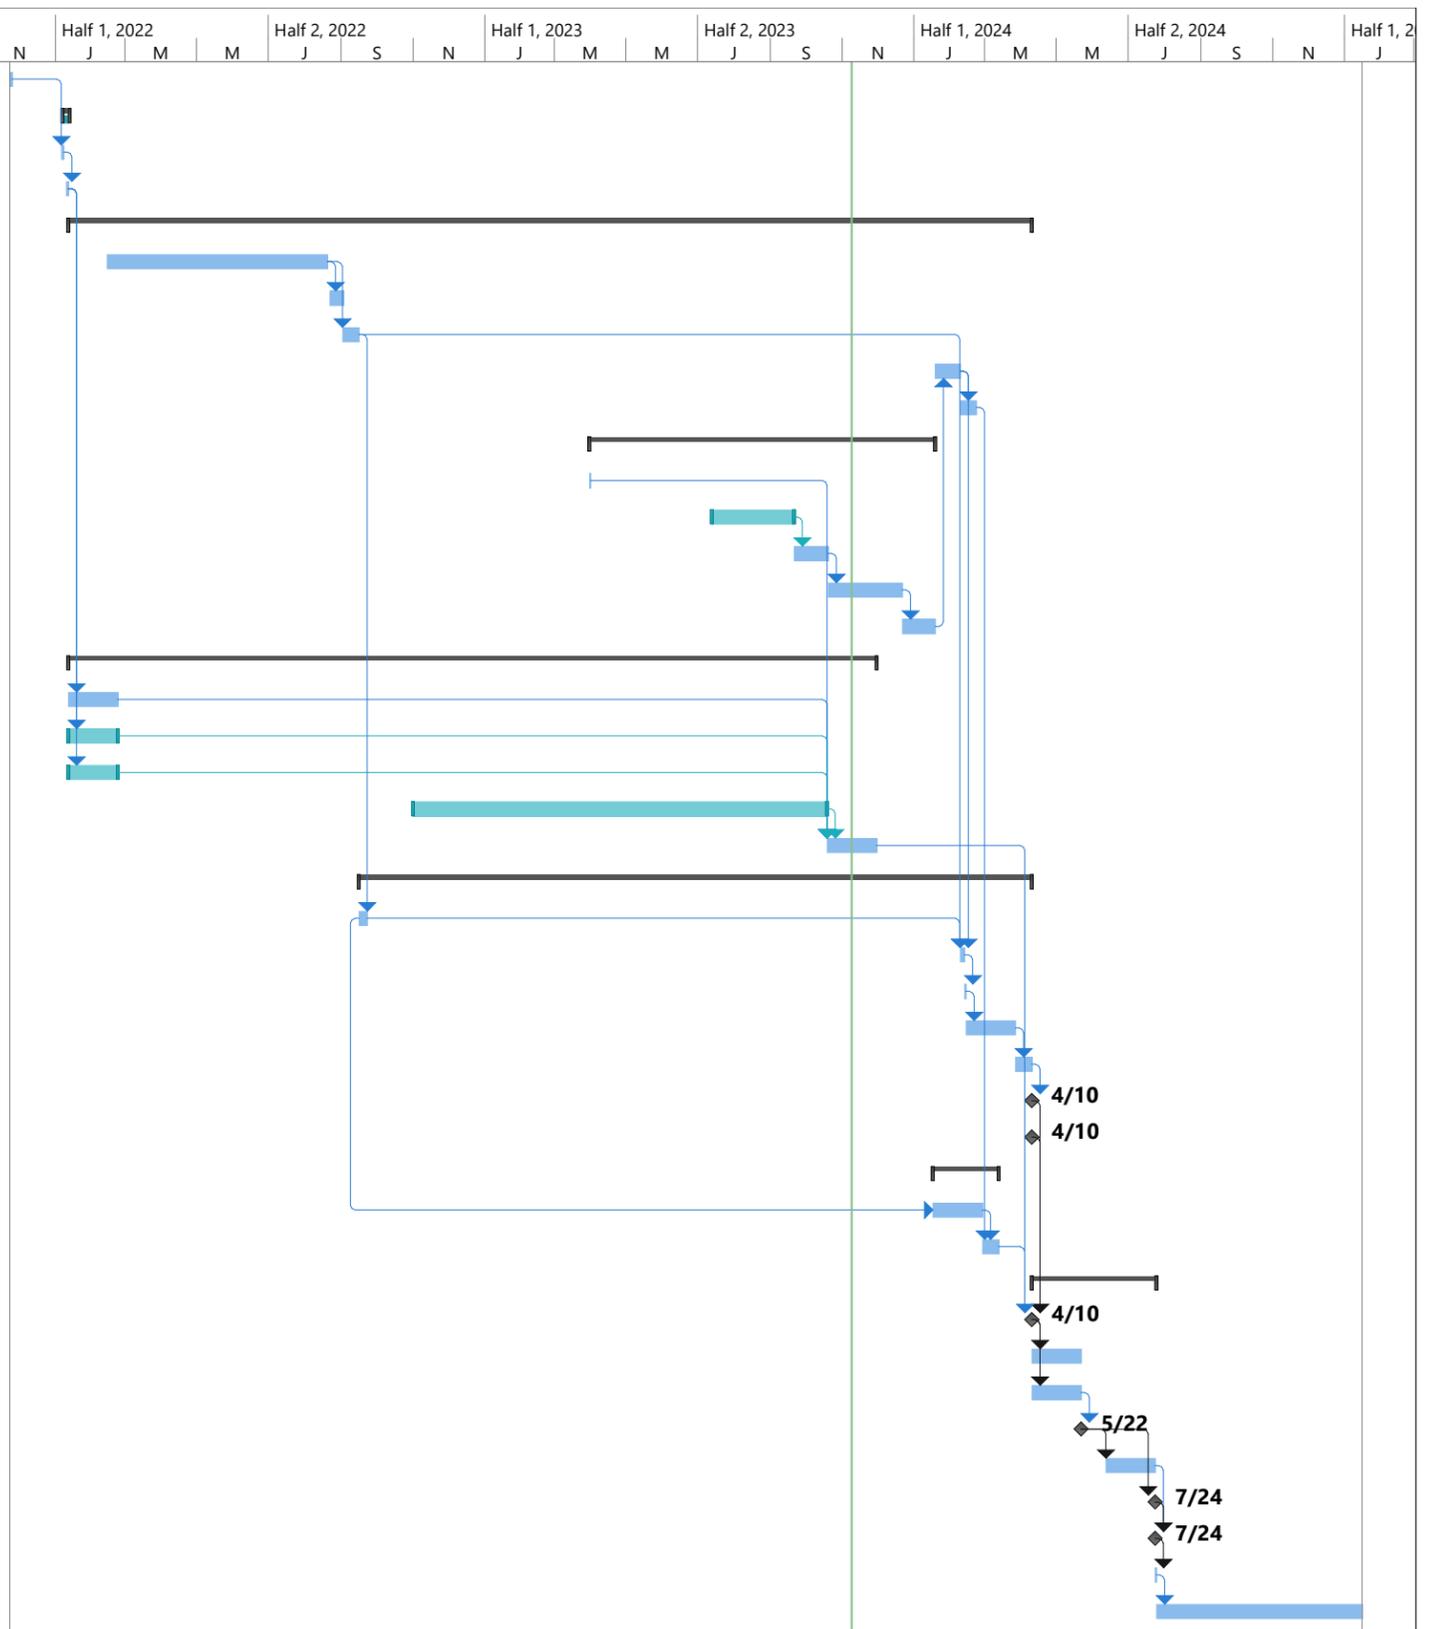

Project: Pocahontas County ARC
Date: Thu 11/9/23

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
